


CONSTRUCTION SCHEDULE EL CONQUISTADOR - TUCSON, AZ

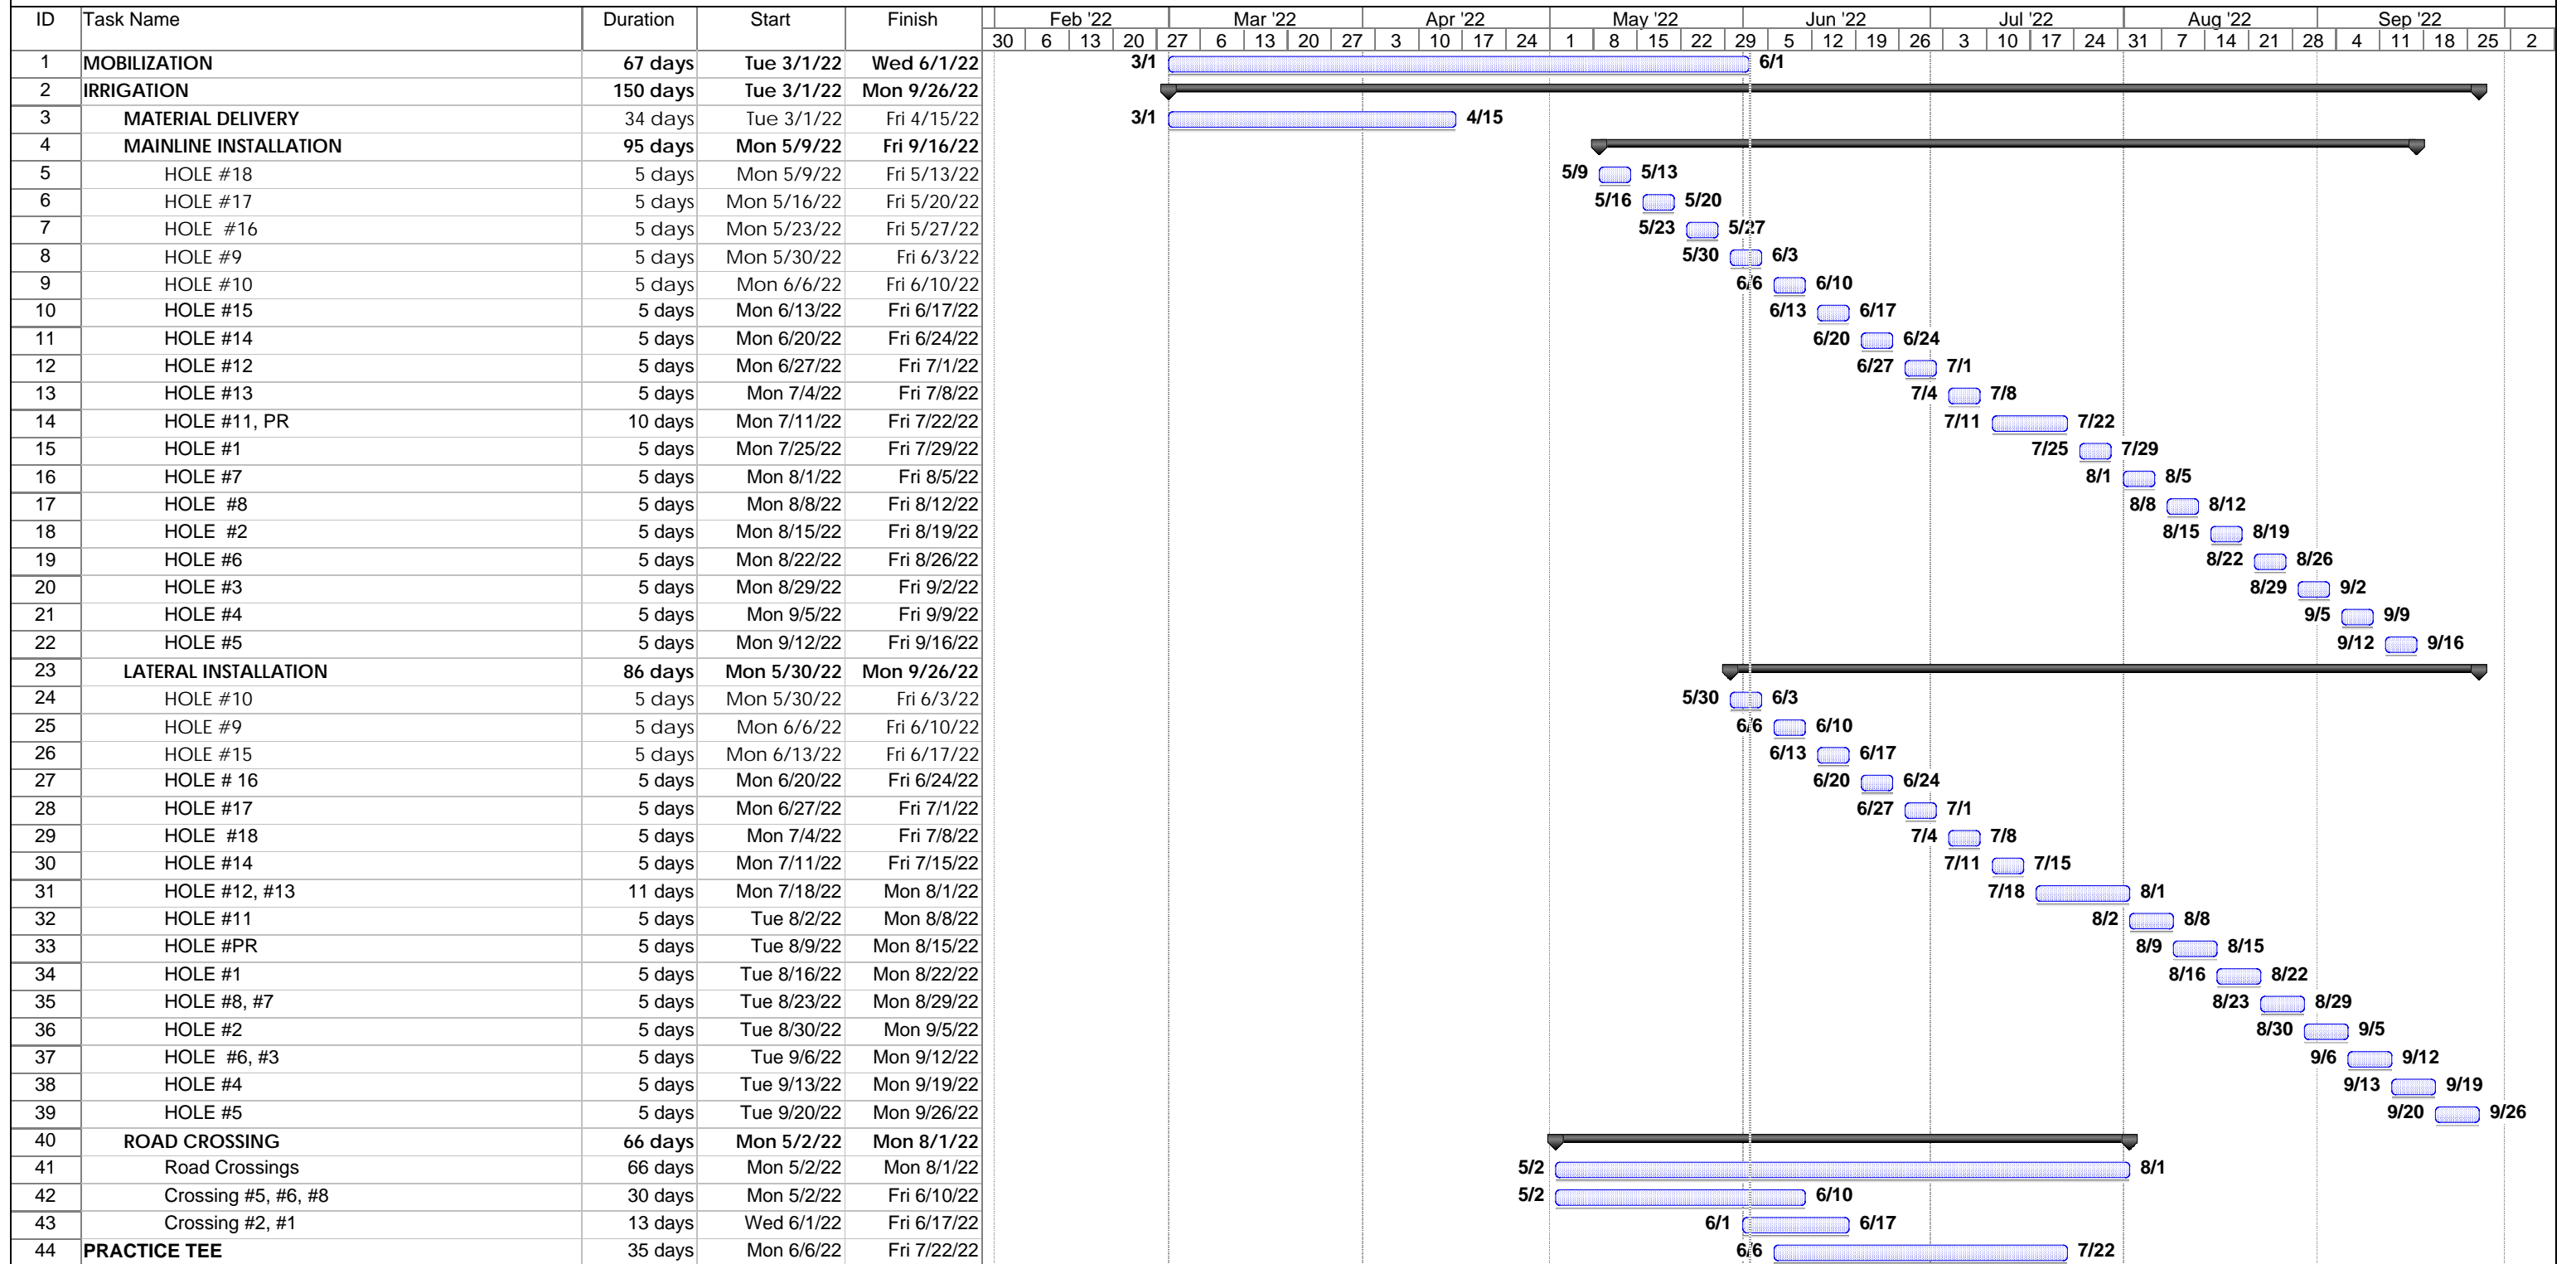

Task		Rolled Up Task		Split		Group By Summary	
Milestone		Rolled Up Milestone		External Tasks		Progress	
Summary		Rolled Up Progress		Project Summary		Deadline	

#	Activity ID	Activity Name	Original Duration	Actual Duration	Remaining Duration	Start	Finish	Calendar																											
								April 2022	May 2022	June 2022	July 2022	August 2022	S	October 2022	N	D	January 2023	F	March 2023	April 2023	May 2023	June 2023	July 2023	August 2023	S	23									
1	Oro Valley Naranja Park - Current		352	49	341	28-Mar-22 A	06-Oct-23																												
2	Milestones		341	1	341	31-May-22 A	06-Oct-23																												
3	Contractual Milestones		341	1	341	31-May-22 A	06-Oct-23																												
4	MS-1100	Milestones - Ground Breaking Ceremony	0	0	0	31-May-22 A																													
5	MS-1000	Milestones - NTP	0	0	0	01-Jun-22 A																													
6	MS-1090	Milestones - Construction Start	0	0	0	06-Jun-22																													
7	MS-1080	Milestones - Certificate of Occupancy	0	0	0		08-Sep-23																												
8	MS-1010	Milestones - Substantial Completion	0	0	0		15-Sep-23																												
9	MS-1020	Milestones - Project Complete	0	0	0		06-Oct-23																												
10	Project Milestones		0	0	0																														
11	Owner Activities		0	0	0																														
12	Preconstruction		0	0	0																														
13	Design - GMP 1-4		127	49	116	28-Mar-22 A	16-Nov-22																												
14	DES-1000	Design - Phase 1 - GMP-1 Mass Grading 75%	20	24	0	28-Mar-22 A	29-Apr-22 A																												
15	DES-1015	Design - Phase 1 - GMP-2 Walkway Improvements	5	29	0	28-Mar-22 A	06-May-22 A																												
16	DES-1005	Design - Phase 1 - GMP-1 Mass Grading 100%	15	9	0	25-Apr-22 A	06-May-22 A																												
17	DES-1020	Design - Phase 3 - GMP-3 Utilities SD	30	19	11	09-May-22 A	20-Jun-22																												
18	DES-1060	Design - Phase 4 - GMP-4 Park Improvements SD	73	19	54	09-May-22 A	19-Aug-22																												
19	DES-1040	Design - Phase 3 - GMP-3 Utilities 75%	30	0	30	21-Jun-22	02-Aug-22																												
20	DES-1050	Design - Phase 3 - GMP-3 Utilities 100%	27	0	27	03-Aug-22	09-Sep-22																												
21	DES-1070	Design - Phase 4 - GMP-4 Park Improvements 75%	33	0	33	22-Aug-22	06-Oct-22																												
22	DES-1080	Design - Phase 4 - GMP-4 Park Improvements 100%	29	0	29	07-Oct-22	16-Nov-22																												
23	Permitting GMP 1-4		142	10	131	02-May-22 A	09-Dec-22																												
24	PER-1000	Permitting - GMP- 1 Mass Grading Permit Submittal & Approval	5	10	0	02-May-22 A	16-May-22 A																												
25	PER-1010	Permitting - GMP- 2 Existing Fields Walkway Improvements	5	0	5	06-Jun-22	10-Jun-22																												
26	PER-1020	Permitting - GMP- 3 Utilities Permit Submittal & Approval	10	0	10	12-Sep-22	23-Sep-22																												
27	PER-1040	Permitting - GMP- 4 Park Improvements Permit Submittal & Approval	15	0	15	17-Nov-22	09-Dec-22																												
28	Procurement		260	0	260	06-Jun-22	13-Jun-23																												
29	Construction		316	9	316	23-May-22 A	31-Aug-23																												
30	GMP 1 - Mass Grading		103	9	103	23-May-22 A	28-Oct-22																												
31	Mobilize/Make Ready		9	8	7	23-May-22 A	15-Jun-22																												
32	MOB-1000	Mobilize	9	8	0	23-May-22 A	03-Jun-22 A																												
33	MOB-1010	Site Fencing and Controls	5	3	0	24-May-22 A	27-May-22 A																												
34	MOB-1030	Set Up Field Office	2	0	2	07-Jun-22	08-Jun-22																												
35	MOB-1040	Utilities to Site Office	5	0	5	09-Jun-22	15-Jun-22																												
36	Civil - Mass Grading		70	3	70	01-Jun-22 A	13-Sep-22																												
37	CIV-1010	Civil - Clear & Grub	5	3	2	01-Jun-22 A	07-Jun-22																												
38	CIV-1020	Civil - Install SWWWP	7	0	7	06-Jun-22 A	14-Jun-22																												
39	CIV-1040	Civil - Site Earthwork Mass Grading	65	0	65	13-Jun-22	13-Sep-22																												
40	CIV-1050	Civil - Musette North - Grading / Build Berm - Cuts/Fills	8	0	8	13-Jun-22	22-Jun-22																												
41	CIV-1060	Civil - Northeast Corner Fill	8	0	8	13-Jun-22	22-Jun-22																												
42	CIV-1080	Civil - New Dog Park Fill	34	0	34	20-Jun-22	05-Aug-22																												
43	CIV-1070	Civil - New Dog Park Cut	31	0	31	23-Jun-22	05-Aug-22																												
44	CIV-1090	Civil - North Fields Fill	31	0	31	23-Jun-22	05-Aug-22																												
45	CIV-1100	Civil - East Slope Cut	31	0	31	23-Jun-22	05-Aug-22																												
46	CIV-1110	Civil - East Slope Fill	36	0	36	23-Jun-22	12-Aug-22																												
47	CIV-1120	Civil - West Slope Cut	29	0	29	01-Aug-22	09-Sep-22																												
48	CIV-1160	Civil - South Fields Fill	29	0	29	01-Aug-22	09-Sep-22																												
49	CIV-1130	Civil - West Slope Fill	29	0	29	01-Aug-22	09-Sep-22																												
50	Musette Dr. Road Work		90	0	90	23-Jun-22	28-Oct-22																												
51	Dog Park Fine Grading		0	0	0																														
52	GMP 2 - Walkway Improvements		51	0	51	01-Jul-22	13-Sep-22																												
53	Walkway Improvements		51	0	51	01-Jul-22	13-Sep-22																												
54	WI-1000	Walkway - Private Blue Stake / Pothole	5	0	5	01-Jul-22	08-Jul-22																												
55	WI-1005	Walkway - Demo & Site Prep	2	0	2	11-Jul-22	12-Jul-22																												
56	WI-1010	Walkway - Grading	10	0	10	12-Jul-22	25-Jul-22																												
57	WI-1020	Walkway - Storm Drain & Catch Basins	10	0	10	18-Jul-22	29-Jul-22																												
58	WI-1110	Walkway - Shade Canopies Footings	5	0	5	26-Jul-22	01-Aug-22																												
59	WI-1150	Walkway - UG Electric	5	0	5	26-Jul-22	01-Aug-22																												
60	WI-1070	Walkway - Landscape Irrigation	5	0	5	01-Aug-22	05-Aug-22																												
61	WI-1050	Walkway - Seat Wall 3 Retaining Wall	5	0	5	02-Aug-22	08-Aug-22																												
62	WI-1060	Walkway - Sidewalk Placement	10	0	10	02-Aug-22	15-Aug-22																												
63	WI-1040	Walkway - Seat Wall 2	5	0	5	09-Aug-22	15-Aug-22																												

- █ Actual Work
- █ Remaining Work
- █ Critical Remaining Work
- ◆ Milestone
- Summary



Oro Valley Naranja Park Expansion

Master Update 06-Jun-22

1 of 2

#	Activity ID	Activity Name	Original Duration	Actual Duration	Remaining Duration	Start	Finish	April 2022	May 2022	June 2022	July 2022	August 2022	S	October 2022	N	D	January 2023	F	March 2023	April 2023	May 2023	June 2023	July 2023	August 2023	S	23																																			
								03	10	17	2	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06
64	WI-1100	Walkway - Concrete Headers	5	0	5	09-Aug-22	15-Aug-22																																																						
65	WI-1030	Walkway - Seat Wall 1	5	0	5	16-Aug-22	22-Aug-22																																																						
66	WI-1080	Walkway - Landscape Planting	5	0	5	16-Aug-22	22-Aug-22																																																						
67	WI-1120	Walkway - Shade Canopies	5	0	5	23-Aug-22	29-Aug-22																																																						
68	WI-1140	Walkway - Landscape Mulch & Stabilized DG	5	0	5	23-Aug-22	29-Aug-22																																																						
69	WI-1160	Walkway - Electric Trim	5	0	5	23-Aug-22	29-Aug-22																																																						
70	WI-1090	Walkway - Benches & Drinking Fountains Instal	5	0	5	30-Aug-22	06-Sep-22																																																						
71	WI-1170	Walkway - Clean & Punch	5	0	5	07-Sep-22	13-Sep-22																																																						
72	GMP 3 - Utilities		226	0	226	06-Jun-22	25-Apr-23																																																						
73	Utilities		226	0	226	06-Jun-22	25-Apr-23																																																						
74	GMP 4 - Park Features		185	0	185	12-Dec-22	31-Aug-23																																																						
75	Project Closeout		25	0	25	01-Sep-23	06-Oct-23																																																						
76	Inspections		5	0	5	01-Sep-23	08-Sep-23																																																						
77	Punch/Admin		25	0	25	01-Sep-23	06-Oct-23																																																						
78	Impacts		0	0	0																																																								
79	Deleted Activities (Actualize as complete on data date and remove all Ic		0	0	0																																																								

Actual Work Remaining Work Critical Remaining Work
 Milestone Summary



ID	Task Name	Duration	Start	Finish	Predecessors	May 2022							June 2022							July 2022							August 2022							September 2022							October 2022						
						16	21	26	1	6	11	16	21	26	31	5	10	15	20	25	30	5	10	15	20	25	30	4	9	14	19	24	29	3	8	13	18	23	28	3	8	13	18	23			
1	Town of Oro Valley Tennis & Pickleball Courts	183.38 e...	Thu 4/21/22	Fri 10/21/22																																											
2	Notice to Proceed on Contract	1 day	Thu 4/21/22	Thu 4/21/22																																											
3	Submittal Phase	7 days	Fri 4/22/22	Mon 5/2/22	2																																										
4	Construction Phase	165.38 e...	Mon 5/9/22	Fri 10/21/22																																											
5	Onsite Mobilization	1 day	Mon 5/9/22	Mon 5/9/22																																											
6	Construction Restrooms	1 day	Mon 5/9/22	Mon 5/9/22	3																																										
7	Dumpster	1 day	Mon 5/9/22	Mon 5/9/22	3																																										
8	Temporary Fencing	1 day	Mon 5/9/22	Mon 5/9/22	3																																										
9	Demolition & Site Prep	106.13 d...	Thu 5/19/22	Fri 10/14/22																																											
10	Demo existing courts, footers and fence	2 wks	Thu 5/19/22	Wed 6/1/22	8																																										
11	Grading and drainage	2 wks	Thu 6/2/22	Wed 6/15/22	10																																										
12	Prep Swales and aprons	1 day	Thu 5/19/22	Thu 5/19/22																																											
13	Underground Utilities-Drainage pipe & Bubbler	1 wk	Thu 6/16/22	Wed 6/22/22	11																																										
14	Utility trench	1 wk	Thu 6/16/22	Wed 6/22/22	11																																										
15	Electrical Demo	2 wks	Thu 5/19/22	Wed 6/1/22	8																																										
16	Concrete & Retaining walls	85 days	Thu 6/2/22	Wed 9/28/22																																											
17	Fill and compact AB for sidewalks	3 days	Mon 9/26/22	Wed 9/28/22	22																																										
18	Footings and rebar for retaining walls	4 days	Thu 6/2/22	Tue 6/7/22	15																																										
19	Inspections	1 day	Wed 6/8/22	Wed 6/8/22	18																																										
20	AB for slabs and compaction testing	1 wk	Wed 6/15/22	Tue 6/21/22																																											
21	Construct Retaining walls	2 wks	Thu 6/9/22	Wed 6/22/22	19																																										
22	Form new sidewalks, stairs ramps	2 mons	Mon 8/1/22	Fri 9/23/22																																											
23	Pour sidewalks, stairs and ramps	2 mons	Mon 8/1/22	Fri 9/23/22																																											
24	Install Sand for PT Slabs Fine Grade	1 wk	Mon 6/13/22	Fri 6/17/22																																											
25	Caulk joints	3 days	Mon 8/29/22	Wed 8/31/22																																											
26	PT Slabs	80 days	Mon 6/20/22	Fri 10/7/22																																											
27	Set forms & Sleeves	2 mons	Mon 6/13/22	Fri 8/5/22																																											
28	Plastic & PT Cables	2 mons	Tue 6/28/22	Mon 8/22/22																																											
29	Pour	2 mons	Wed 6/29/22	Tue 8/23/22																																											

Oro Valley Tennis & Pickleball Renovation	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
	Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Name	Duration	Start	Finish	Predecessors	May 2022							June 2022							July 2022							August 2022							September 2022							October 2022						
						16	21	26	1	6	11	16	21	26	31	5	10	15	20	25	30	5	10	15	20	25	30	4	9	14	19	24	29	3	8	13	18	23	28	3	8	13	18	23	28		
30	Fencing	2 mons	Thu 7/14/22	Wed 9/7/22																																											
31	Surfacing	2 mons	Mon 8/15/22	Fri 10/7/22																																											
32	Drainage Improvments & Irrigation	69 days?	Thu 6/16/22	Tue 9/20/22																																											
33	Move irrigation heads	3 wks	Tue 8/23/22	Mon 9/12/22	28																																										
34	Drain Sump for drinking fountain	1 day?	Thu 6/16/22	Thu 6/16/22	11																																										
35	Install RIP Rap in drainage areas	1 wk	Tue 9/13/22	Mon 9/19/22	33																																										
36	New Drinking fountain and bottle fill	1 day	Tue 9/20/22	Tue 9/20/22	35																																										
37	Shade & Canopies	68 days	Mon 6/13/22	Wed 9/14/22																																											
38	Shade footings	1 day	Tue 8/23/22	Tue 8/23/22	28																																										
39	Raise Existing shade columns	1 wk	Mon 6/13/22	Fri 6/17/22																																											
40	Shade Columns	1 day	Tue 8/23/22	Tue 8/23/22	28																																										
41	Shade Canopies	1 day	Wed 9/14/22	Wed 9/14/22																																											
42	ELECTRICAL	30 days	Wed 6/8/22	Tue 7/19/22																																											
43	Electrical underground	1 wk	Wed 6/8/22	Tue 6/14/22																																											
44	Remove conduit and wiring back to recep and boxes	1 wk	Wed 6/15/22	Tue 6/21/22	43																																										
45	Run new wiring to existing fixtures an receps	1 wk	Wed 6/22/22	Tue 6/28/22	44																																										
46	Install light pole fixtures and GFI's	1 wk	Wed 6/29/22	Tue 7/5/22	45																																										
47	Complete work to existing panels	2 wks	Wed 7/6/22	Tue 7/19/22	46																																										
48	SITE AMENITIES	50 days?	Mon 6/20/22	Fri 8/26/22																																											
49	Fencing	4 wks	Mon 6/20/22	Fri 7/15/22																																											
50	Handrail at steps and retaining wall and ramp	1 wk	Mon 8/15/22	Fri 8/19/22																																											
51	Install Drinking Fountain & bottle fill	1 wk	Mon 8/22/22	Fri 8/26/22																																											
52	Project Completion	11 days?	Fri 10/7/22	Fri 10/21/22																																											
53	Certificate of Substantial Completion	1 day	Fri 10/7/22	Fri 10/7/22																																											
54	Punch List	2 wks	Fri 10/7/22	Thu 10/20/22																																											
55	Certificate of Final Completion	1 day	Mon 10/10/22	Mon 10/10/22	53																																										
56	Final Pay Application	1 day	Mon 10/10/22	Mon 10/10/22	53																																										
57	Warranties and O&M	2 wks	Mon 10/10/22	Fri 10/21/22	53																																										

Oro Valley Tennis & Pickleball Renovation	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
	Summary		Inactive Task		Duration-only		Finish-only			
