

- █ Actual Work
- █ Remaining Work
- █ Critical Remaining Work
- ◆ Milestone
- Summary



ORO VALLEY - NARANJA PARK EXPANSION

Master Update 19-May-22

ID	Task Name	Duration	Start	Finish	Predecessors	May 2022							June 2022							July 2022							August 2022							September 2022							October 2022						
						16	21	26	1	6	11	16	21	26	31	5	10	15	20	25	30	5	10	15	20	25	30	4	9	14	19	24	29	3	8	13	18	23	28	3	8	13	18	23			
1	<b>Town of Oro Valley Tennis &amp; Pickleball Courts</b>	<b>183.38 e...</b>	<b>Thu 4/21/22</b>	<b>Fri 10/21/22</b>																																											
2	Notice to Proceed on Contract	1 day	Thu 4/21/22	Thu 4/21/22																																											
3	Submittal Phase	7 days	Fri 4/22/22	Mon 5/2/22	2																																										
4	<b>Construction Phase</b>	<b>165.38 e...</b>	<b>Mon 5/9/22</b>	<b>Fri 10/21/22</b>																																											
5	Onsite Mobilization	1 day	Mon 5/9/22	Mon 5/9/22																																											
6	Construction Restrooms	1 day	Mon 5/9/22	Mon 5/9/22	3																																										
7	Dumpster	1 day	Mon 5/9/22	Mon 5/9/22	3																																										
8	Temporary Fencing	1 day	Mon 5/9/22	Mon 5/9/22	3																																										
9	<b>Demolition &amp; Site Prep</b>	<b>106.13 d...</b>	<b>Thu 5/19/22</b>	<b>Fri 10/14/22</b>																																											
10	Demo existing courts, footers and fence	2 wks	Thu 5/19/22	Wed 6/1/22	8																																										
11	Grading and drainage	2 wks	Thu 6/2/22	Wed 6/15/22	10																																										
12	Prep Swales and aprons	1 day	Thu 5/19/22	Thu 5/19/22																																											
13	Underground Utilities-Drainage pipe & Bubbler	1 wk	Thu 6/16/22	Wed 6/22/22	11																																										
14	Utility trench	1 wk	Thu 6/16/22	Wed 6/22/22	11																																										
15	Electrical Demo	2 wks	Thu 5/19/22	Wed 6/1/22	8																																										
16	<b>Concrete &amp; Retaining walls</b>	<b>65 days</b>	<b>Thu 6/2/22</b>	<b>Wed 8/31/22</b>																																											
17	Fill and compact AB for sidewalks	3 days	Thu 6/2/22	Mon 6/6/22	15																																										
18	Footings and rebar for retaining walls	4 days	Thu 6/2/22	Tue 6/7/22	15																																										
19	Inspections	1 day	Wed 6/8/22	Wed 6/8/22	18																																										
20	AB for slabs and compaction testing	1 wk	Mon 6/6/22	Fri 6/10/22																																											
21	Construct Retaining walls	2 wks	Thu 6/9/22	Wed 6/22/22	19																																										
22	Form new sidewalks, stairs ramps	3 days	Tue 6/7/22	Thu 6/9/22	17																																										
23	Pour sidewalks, stairs and ramps	2 days	Fri 6/10/22	Mon 6/13/22	22																																										
24	Install Sand for PT Slabs Fine Grade	1 wk	Mon 6/13/22	Fri 6/17/22	20																																										
25	Caulk joints	3 days	Mon 8/29/22	Wed 8/31/22																																											
26	<b>PT Slabs</b>	<b>80 days</b>	<b>Mon 6/20/22</b>	<b>Fri 10/7/22</b>																																											
27	Set forms & Sleeves	2 mons	Mon 6/20/22	Fri 8/12/22	24																																										
28	Plastic & PT Cables	2 mons	Tue 6/28/22	Mon 8/22/22																																											
29	Pour	2 mons	Wed 6/29/22	Tue 8/23/22																																											
30	Fencing	2 mons	Thu 7/14/22	Wed 9/7/22																																											


Town of Oro Valley-Tennis & P Tue 5/24/22	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
	Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Name	Duration	Start	Finish	Predecessors	May 2022	June 2022	July 2022	August 2022	September 2022	October 2022
31	Surfacing	2 mons	Mon 8/15/22	Fri 10/7/22							Surfacing
32	<b>Drainage Improvments &amp; Irrigation</b>	<b>69 days?</b>	<b>Thu 6/16/22</b>	<b>Tue 9/20/22</b>							Drainage Improvments
33	Move irrigation heads	3 wks	Tue 8/23/22	Mon 9/12/22	28						Move irrigation heads
34	Drain Sump for drinking fountain	1 day?	Thu 6/16/22	Thu 6/16/22	11						Drain Sump for drinking fountain
35	Install RIP Rap in drainage areas	1 wk	Tue 9/13/22	Mon 9/19/22	33						Install RIP Rap in drainage
36	New Drinking fountain and bottle fill	1 day	Tue 9/20/22	Tue 9/20/22	35						New Drinking fountain a
37	<b>Shade &amp; Canopies</b>	<b>68 days</b>	<b>Mon 6/13/22</b>	<b>Wed 9/14/22</b>							Shade & Canopies
38	Shade footings	1 day	Tue 8/23/22	Tue 8/23/22	28						Shade footings
39	Raise Existing shade columns	1 wk	Mon 6/13/22	Fri 6/17/22							Raise Existing shade columns
40	Shade Columns	1 day	Tue 8/23/22	Tue 8/23/22	28						Shade Columns
41	Shade Canopies	1 day	Wed 9/14/22	Wed 9/14/22							Shade Canopies
42	<b>ELECTRICAL</b>	<b>30 days</b>	<b>Wed 6/8/22</b>	<b>Tue 7/19/22</b>							
43	Electrical underground	1 wk	Wed 6/8/22	Tue 6/14/22							Electrical underground
44	Remove conduit and wiring back to recep and boxes	1 wk	Wed 6/15/22	Tue 6/21/22	43						Remove conduit and wiring back to recep and boxes
45	Run new wiring to existing fixtures an recepts	1 wk	Wed 6/22/22	Tue 6/28/22	44						Run new wiring to existing fixtures an recepts
46	Install light pole fixtures and GFI's	1 wk	Wed 6/29/22	Tue 7/5/22	45						Install light pole fixtures and GFI's
47	Complete work to existing panels	2 wks	Wed 7/6/22	Tue 7/19/22	46						Complete work to existing panels
48	<b>SITE AMENITIES</b>	<b>20 days?</b>	<b>Mon 6/20/22</b>	<b>Fri 7/15/22</b>							
49	Fencing	4 wks	Mon 6/20/22	Fri 7/15/22							Fencing
50	Handrail at steps and retaining wall and ramp	1 wk	Mon 6/20/22	Fri 6/24/22							Handrail at steps and retaining wall and ramp
51	<New Task>	1 day?	Mon 6/20/22	Mon 6/20/22							<New Task>
52	Install Drinking Fountain & bottle fill	1 wk	Mon 6/20/22	Fri 6/24/22							Install Drinking Fountain & bottle fill
53		1 wk	Mon 6/20/22	Fri 6/24/22							
54	<b>Project Completion</b>	<b>11 days?</b>	<b>Fri 10/7/22</b>	<b>Fri 10/21/22</b>							
55	Certificate of Substantial Completion	1 day	Fri 10/7/22	Fri 10/7/22	53						Certificate of
56	Punch List	2 wks	Fri 10/7/22	Thu 10/20/22							Punch
57	Certificate of Final Completion	1 day	Mon 10/10/22	Mon 10/10/22	55						Certificate
58	Final Pay Application	1 day	Mon 10/10/22	Mon 10/10/22	55						Final Pay A
59	Warranties and O&M	2 wks	Mon 10/10/22	Fri 10/21/22	55						Warr

Town of Oro Valley-Tennis & P  
Tue 5/24/22

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
Summary		Inactive Task		Duration-only		Finish-only			

## CONSTRUCTION SCHEDULE EL CONQUISTADOR - TUCSON, AZ

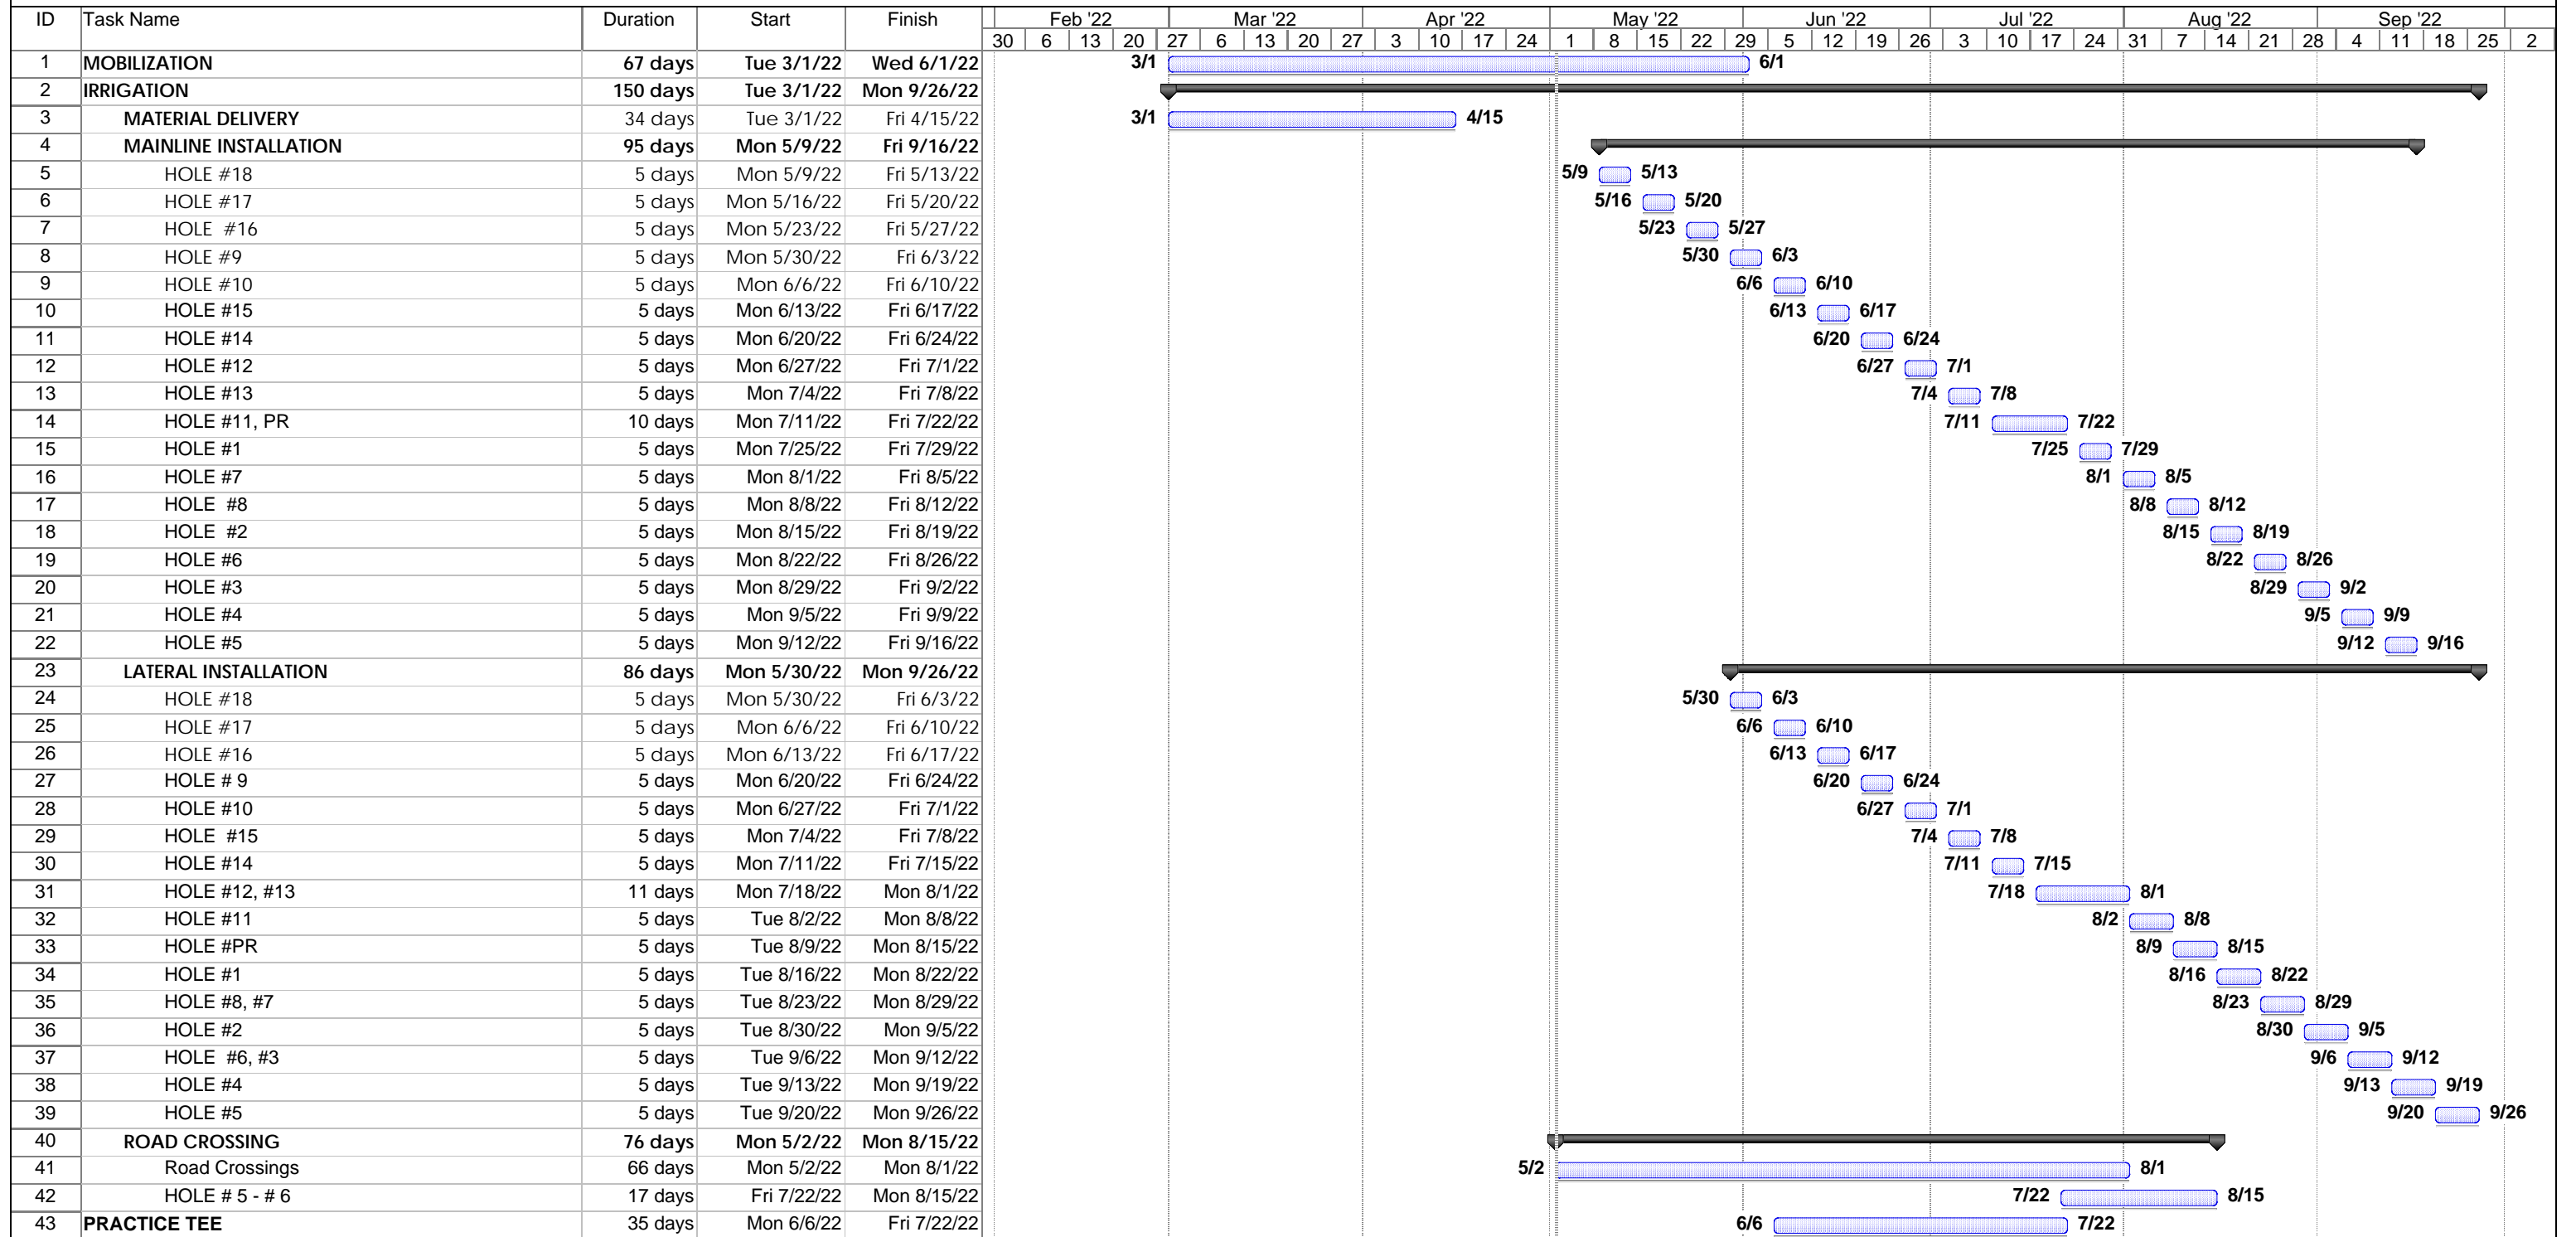

Task		Rolled Up Task		Split		Group By Summary	
Milestone		Rolled Up Milestone		External Tasks		Progress	
Summary		Rolled Up Progress		Project Summary		Deadline	
